










Town of Queen Creek

Capital Improvement Projects Update









Completed	58%	
Active	25%	
Remaining	17%	

10-Year IIP Roadway Projects 2018-2027

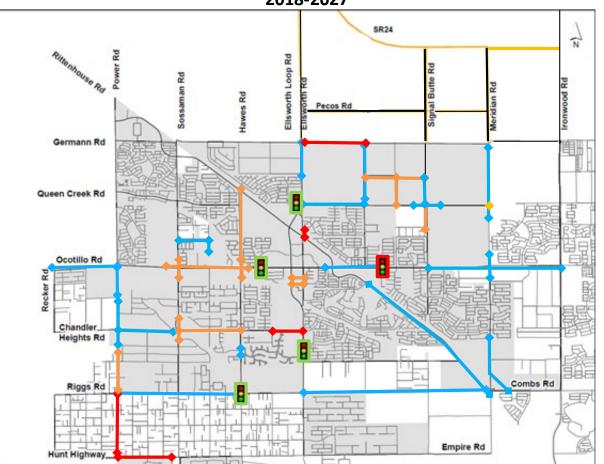

CIP Projects – Non-IIP

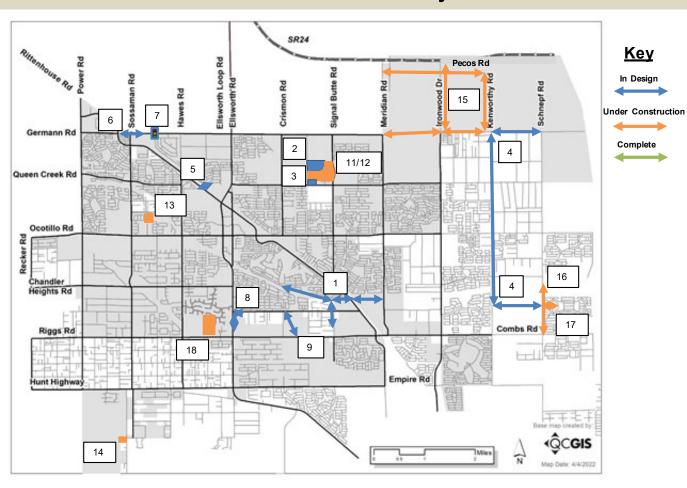

In Design

- Queen Creek Wash Ph1 & 2
- 2. Field Operations Facility
- 3. Public Safety Resource Center
- . Pinal County IGA ARPA Funded Projects
- 5. Rittenhouse / UPRR Sewer Replacement
- 6. Intersection of Sossaman and Germann
- 7. Traffic Signal @ Germann & 196th
- 8. Ellsworth & Cloud Roads
- . Crismon Road Cloud to Riggs

In Construction

- 11. Frontier Family Park
- 12. East Park Aquatic & Multi-Gen Center
- 13. Mans el Carter Park Phase 2
- 14. Bell Road Pump Station
- 15. ASLD Infrastructure
- 16. Schnepf Road Waterline
- 17. Loredo Ranch Drive Waterline
- 18. HPEC RV Dump Stations



Meridian Road at Queen Creek/Pima Road











Meridian Road at Queen Creek/Pima Roads





ITD	ITD	ITD	
Budget	Expended	Encumbered	Available
16,067,554	11,249,988	4,024,732	792,834









Town Center Roadways Aldecoa Drive and Munoz Street



Town Center Roadways Aldecoa Drive and Munoz Street

- Roadway anticipated completion 1/31/24
- Electrical completion is delayed until May 2024



11,056,357

3,853,744






Ocotillo Road: Sossaman to Hawes










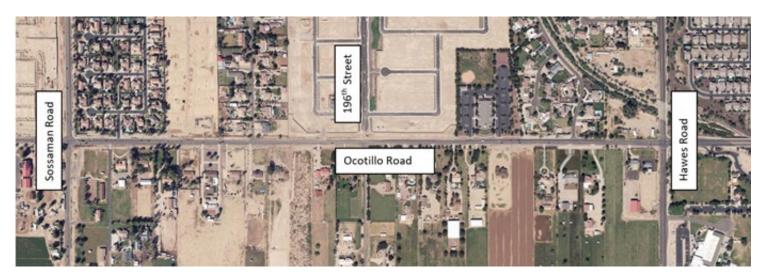

Ocotillo Road: Sossaman to Hawes

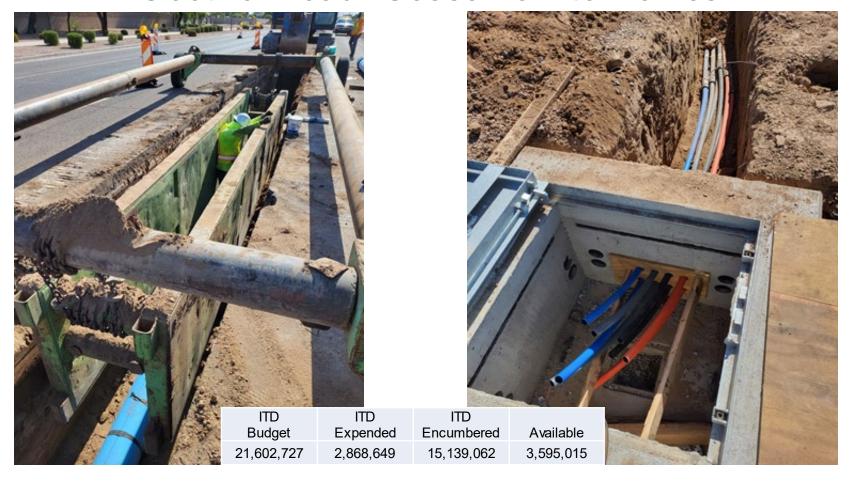

Mansel Carter Phase 2

- Mass grading complete.
- On track for March 1 opening.



ITD Expended 659,348

ITD Encumbered 11,020,368

Available 821,284

Frontier Family Park

- Frontier Family Park Construction ongoing, just over 50% complete.
- Trying to manage through schedule challenges.
- Anticipate opening in late April 2024.



Aquatic and Recreation Center

- Recreation Center building permit issued, waiting on Aquatic Center Permit.
- Underground utilities and building footings under construction.













Other Projects:

- Signal Butte Road from Ocotillo Road to Queen Creek Road
 - Installation of SRP and CenturyLink conduits nearing completion.
 - Storm drain installation is ongoing.
- Queen Creek Road and Hawes Road Interim Signal
 - Complete
 - Final intersection design is ongoing.
- Crismon Road from Riggs Road to Cloud Road
 (Adia a matter Original of Links Cale and)

(Adjacent to Crismon High School)

Contractor is completing pricing for phase 1 improvements. Coordinating with school on timing for construction start.











Questions?
