










Town of Queen Creek

Capital Improvement Projects Update









Completed	58%
Active	25%
Remaining	17%

10-Year IIP Roadway Projects 2018-2027

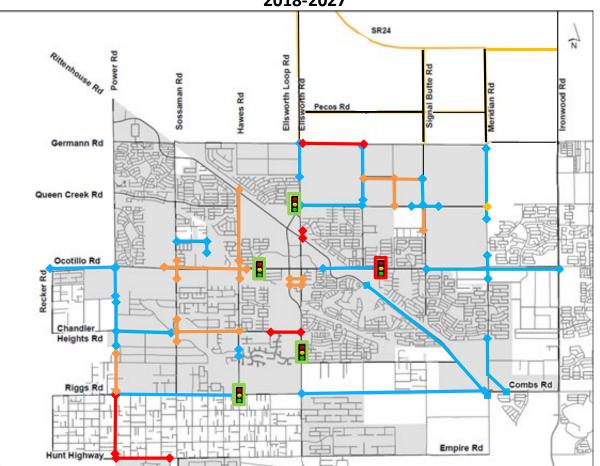

CIP Projects – Non-IIP

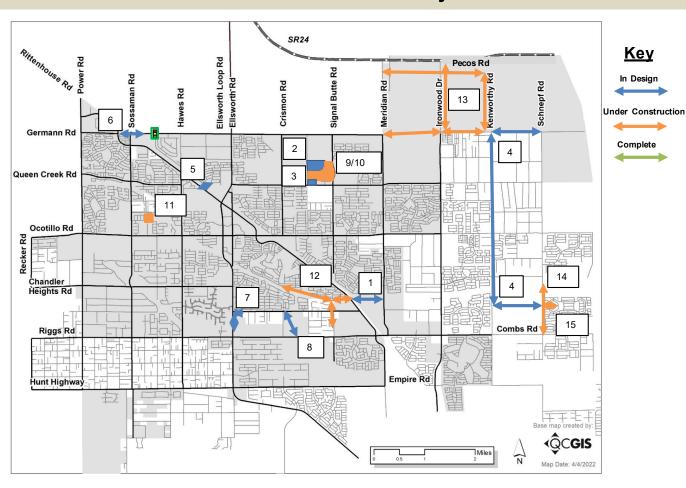

In Design

- 1. Queen Creek Wash Phase 2
- New Fleet Building
- 3. Public Safety Resource Center
- . Pinal County IGA ARPA Funded Projects
- 5. Rittenhouse / UPRR Sewer Replacement
- 6. Intersection of Sossaman and Germann
- Ellsworth & Cloud Roads
- 3. Crismon Road—Cloud to Riggs

In Construction

- 9. Frontier Family Park
- 10. East Park Aquatic & Multi-Gen Center
- 11. Mans el Carter Park Phase 2
- 12. Queen Creek Wash Phase 1
- 13. ASLD Infrastructure
- 14. Schnepf Road Waterline
- 15. Loredo Ranch Drive Waterline

Completed

• Traffic Signal @ Germann & 196th



Meridian Road at Queen Creek/Pima Roads












Meridian Road at Queen Creek/Pima Roads



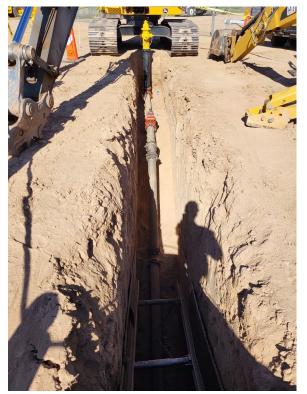

ITD	ITD	ITD	
Budget	Expended	Encumbered	Available
18,004,705	12,092,650	5,336,357	575,698









Town Center Roadways Aldecoa Drive and Munoz Street



Town Center Roadways Aldecoa Drive and Munoz Street





ITD	ITD	ITD	
Budget	Expended	Encumbered	Available
13,159,109	6,482,729	6,854,529	(178, 150)



Ocotillo Road: Sossaman to Hawes











Ocotillo Road: Sossaman to Hawes





ITD	ITD	ITD	
Budget	Expended	Encumbered	Available
21,614,986	9,356,881	9,570,335	2,687,770



Signal Butte: Ocotillo to Queen Creek





Signal Butte: Ocotillo to Queen Creek





ITD	ITD	ITD	
Budget	Expended	Encumbered	Available
4,425,115	2,118,044	920,141	1,387,930



Traffic Signal at Germann Rd & 196th Street





Traffic Signal at Germann Rd & 196th Street



1,931,505

889,676

Encumbered 368,215

Available 673,615

Mansel Carter Phase 2



Mansel Carter Phase 2

Frontier Family Park




Frontier Family Park

Aquatic and Recreation Center



Aquatic and Recreation Center

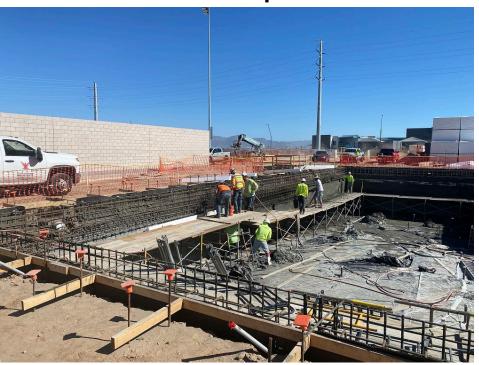



ITD	ITD	ITD	
Budget	Expended	Encumbered	Available
68,000,000	18,700,233	46,857,617	2,442,149

ASLD Infrastructure

Phase 1 Utilities


All mainline is complete.

Working on hydrants and cathodic protection for Ironwood.

Phase 2

Pecos Road water and sewer is complete.

Starting Kenworthy sewer.

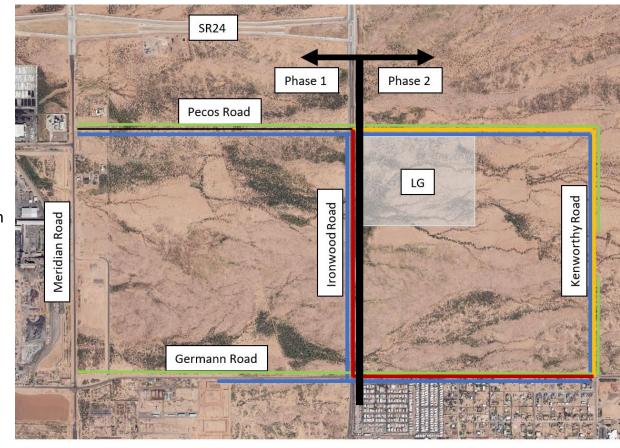

Sewer Improvements	
Water Improvements	
New Roadway	
Roadway Widening	

LG – Site Development





LG – Site Development













Questions?
